

**Camden County Department of Public Works
Division of Engineering
Haddon Avenue (CR 561) Improvements from Euclid
Avenue to Newton Avenue (CR 604), Camden City, Camden County, NJ
County Project No. B1-2025
Project Number: 0400X197
Progress Report No. 03
October 13, 2025 – October 24, 2025**



Figure 1: View of temporary parking sign installed at Walnut Ave

Work Completed Period of October 13, 2025 – October 24, 2025

- Pipe Cleaning and lining along the project corridor
- Reviewing of CCTV video and plan review for proposed pipelining operations



Figure 2: View of manhole being vented

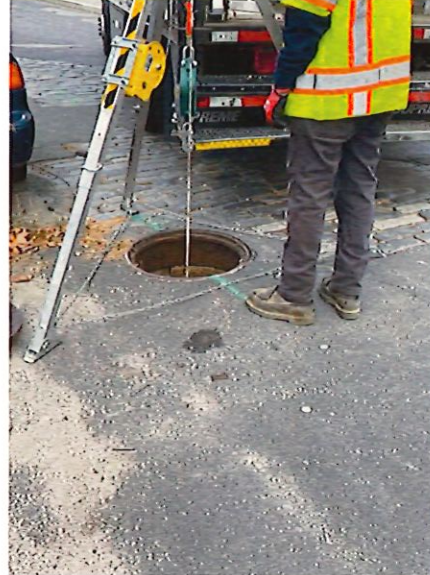
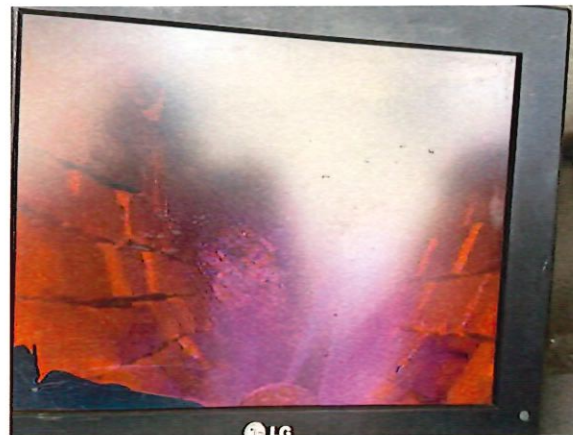


Figure 3: View of attendant at manhole while debris is removed by occupant



Figure 4: View of camera completing 15' pipe segment inspection



*Figure 5:
View of debris being jetted back to manhole*

Quantities Period of October 13, 2025 – October 24, 2025

- Item #13a: Traffic Director, Flagger (59.00 Hours)
- Item #13b: Traffic Director, Flagger (2.00 Hours)

Summary of Work Completed Period of October 13, 2025 – October 24, 2025

Over this period of work, the contractor continued pipe cleaning and measurement areas along the project corridor. The contractor also reviewed CCTV video of the pipes and planned review for proposed pipe planning operations.

General cleanup of the work area was performed after each day. Police traffic directors were utilized during the day's work for traffic control safety measures. Advanced warning signs were used in setting up traffic control safety measures during this period of work.

Anticipated Work for Period of October 27, 2025 – November 7, 2025

- Pipe Clean/Obtain Liner Measurements/Procure Materials

Notice to Proceed: August 25, 2025

Substantial Completion: February 10, 2027

Final Completion: June 27, 2027

Prepared By:

Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
