

**Camden County Department of Public Works
Division of Engineering
Haddon Avenue (CR 561) Improvements from Euclid
Avenue to Newton Avenue (CR 604), Camden City, Camden County, NJ
County Project No. B1-2025
Project Number: 0400X197
Progress Report No. 05
November 11, 2025 – November 21, 2025**



Figure 1: View of manhole being lined

Work Completed Period of November 11, 2025 – November 21, 2025

- Pipelining and Manhole Lining.
- Detour in place for construction between Newton Ave to Kaighns Ave.
- Concrete roadway removal on Haddon Ave from Newton Ave to Kaighns Ave.



Figure 2: View of the inverted liner before curing

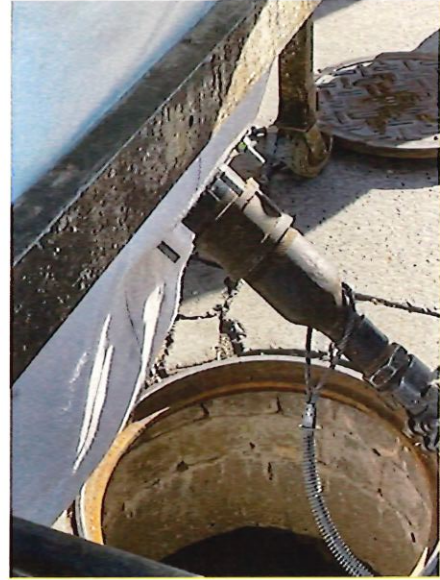


Figure 3: View of liner material being prepped in the inversion machine



Figure 4: View of yellow lines being temporarily removed



Figure 5:
View of the manhole after lining

Quantities Period of November 11, 2025 – November 21, 2025

- Item #13a: Traffic Director, Flagger (389.50 HR)
- Item #16a: Removal of Pavement (1941.00 SY)

- Item #42a: Inlet Filter Type 2, 2' X 4' (2.00 Units)
- Item #56a: Reset Existing Casting (1.00 Units)
- Item #59a: Pipe Lining (20"X30") (130.00 LF)
- Item #64a: Pipe Lining (12") (42.00 LF)
- Item #65a: Pipe Lining (15") (132.00 LF)
- Item #S9a: Manhole Lining (17.00 UN)
- Item #7b: Drum (61.00 UN)
- Item #8b: Traffic Cone (39.00 UN)
- Item #9b: Construction Signs (564.75 UN)

Summary of Work Completed Period of November 11, 2025 – November 21, 2025

Over this period of work, the contractor began with the manhole lining process and pipelining of proposed sanitary sewer lines, which was performed by US Pipe. Temporary removal and shifting of traffic lines was performed to maintain open traffic flow through Phase A of the project while removal of existing concrete roadway was being executed. Concrete roadway removal procedures involve the controlled demolition and extraction of existing pavement to prepare the site for reconstruction and utility work. Prior to removal, the work area is secured with appropriate traffic control, signage, and safety measures to protect workers and the public. Existing utilities are identified and protected to prevent damage. General cleanup of the work area was performed at the end of each day. Police traffic directors were utilized during the day's work for traffic control safety measures.

Anticipated Work for Period of November 24, 2025 – December 5, 2025


- Concrete roadway removal on Haddon Ave.
- Pipelining and Manhole Lining.

Notice to Proceed: August 25, 2025

Substantial Completion: February 10, 2027

Final Completion: June 27, 2027

Prepared By:


Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
